



ID	Task Name	Duration	Start	Finish	Predecessors	Jan 10, '10
1	Milestones	131 days	Wed 3/31/10	Thu 9/30/10		
2	NLR Deployment Plan Complete	0 days	Wed 3/31/10	Wed 3/31/10	9	
3	Design Complete	0 days	Tue 4/6/10	Tue 4/6/10	14	
4	Procurement Complete	0 days	Tue 6/15/10	Tue 6/15/10	19,20,21,22,23,24,25,17	
5	Deployment Complete	0 days	Tue 8/17/10	Tue 8/17/10	30,31,32,33,29	
6	Testing Complete	0 days	Tue 8/24/10	Tue 8/24/10	34	
7	Contingency Date	0 days	Thu 9/30/10	Thu 9/30/10	35	
8	GENI OpenFlow Deployment Schedule	154 days	Mon 3/1/10	Thu 9/30/10		
9	Draft NLR deployment plan for year one	23 days	Mon 3/1/10	Wed 3/31/10		
10	Draft NLR OpenFlow test plan	40 days	Wed 5/5/10	Tue 6/29/10	9	
11	Generate optical engineering design and determine available optic	1 day	Thu 4/1/10	Thu 4/1/10	9	
12	Determine availability of space, power, and cooling	1 day	Fri 4/2/10	Fri 4/2/10	11	
13	Determine availability of FrameNet ports and optics	1 day	Mon 4/5/10	Mon 4/5/10	12	
14	Determine OOB port availability	1 day	Tue 4/6/10	Tue 4/6/10	13	
15	Generate equipment and component lists	5 days	Wed 4/7/10	Tue 4/13/10	14	
16	Order & assign equipment	5 days	Wed 4/14/10	Tue 4/20/10	15	
17	Procure OpenFlow-enabled switches	40 days	Wed 4/21/10	Tue 6/15/10	16	
18	Procure OpenFlow server equipment	40 days	Wed 4/21/10	Tue 6/15/10	16	
19	Procure power equipment	40 days	Wed 4/21/10	Tue 6/15/10	16	
20	Procure transponders & client optics	40 days	Wed 4/21/10	Tue 6/15/10	16	
21	Procure optical chassis (if required)	40 days	Wed 4/21/10	Tue 6/15/10	16	
22	Procure facility rack & power (if required)	40 days	Wed 4/21/10	Tue 6/15/10	16	
23	Procure FrameNet equipment	40 days	Wed 4/21/10	Tue 6/15/10	16	
24	Procure OOB equipment	40 days	Wed 4/21/10	Tue 6/15/10	16	
25	Procure local in-suite cabling	40 days	Wed 4/21/10	Tue 6/15/10	16	
26	Generate external cross-connect orders	10 days	Wed 4/21/10	Tue 5/4/10	14	
27	Generate installation orders	30 days	Wed 5/5/10	Tue 6/15/10	26	
28	Configure OpenFlow controller servers	10 days	Wed 6/16/10	Tue 6/29/10	18	
29	Deploy Sunnyvale system	10 days	Wed 6/16/10	Tue 6/29/10	27,17,19,20,21,22,23,24,25	
30	Deploy Atlanta system	10 days	Wed 7/7/10	Tue 7/20/10	27,17,19,20,21,22,23,24,25,29	
31	Deploy Seattle system	10 days	Wed 7/21/10	Tue 8/3/10	27,17,19,20,21,22,23,24,25,30	
32	Deploy Denver system	5 days	Wed 8/4/10	Tue 8/10/10	27,17,19,20,21,22,23,24,25,31	
33	Deploy Chicago system	5 days	Wed 8/11/10	Tue 8/17/10	27,17,19,20,21,22,23,24,25,32	
34	Test connections and control functions	40 days	Wed 6/30/10	Tue 8/24/10	30FF+5 days,31FF+5 days,32FF+5 c	
35	Project Contingency	27 days	Wed 8/25/10	Thu 9/30/10	34	

Project: GENI Deployment Schedule,
Date: Tue 4/20/10

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

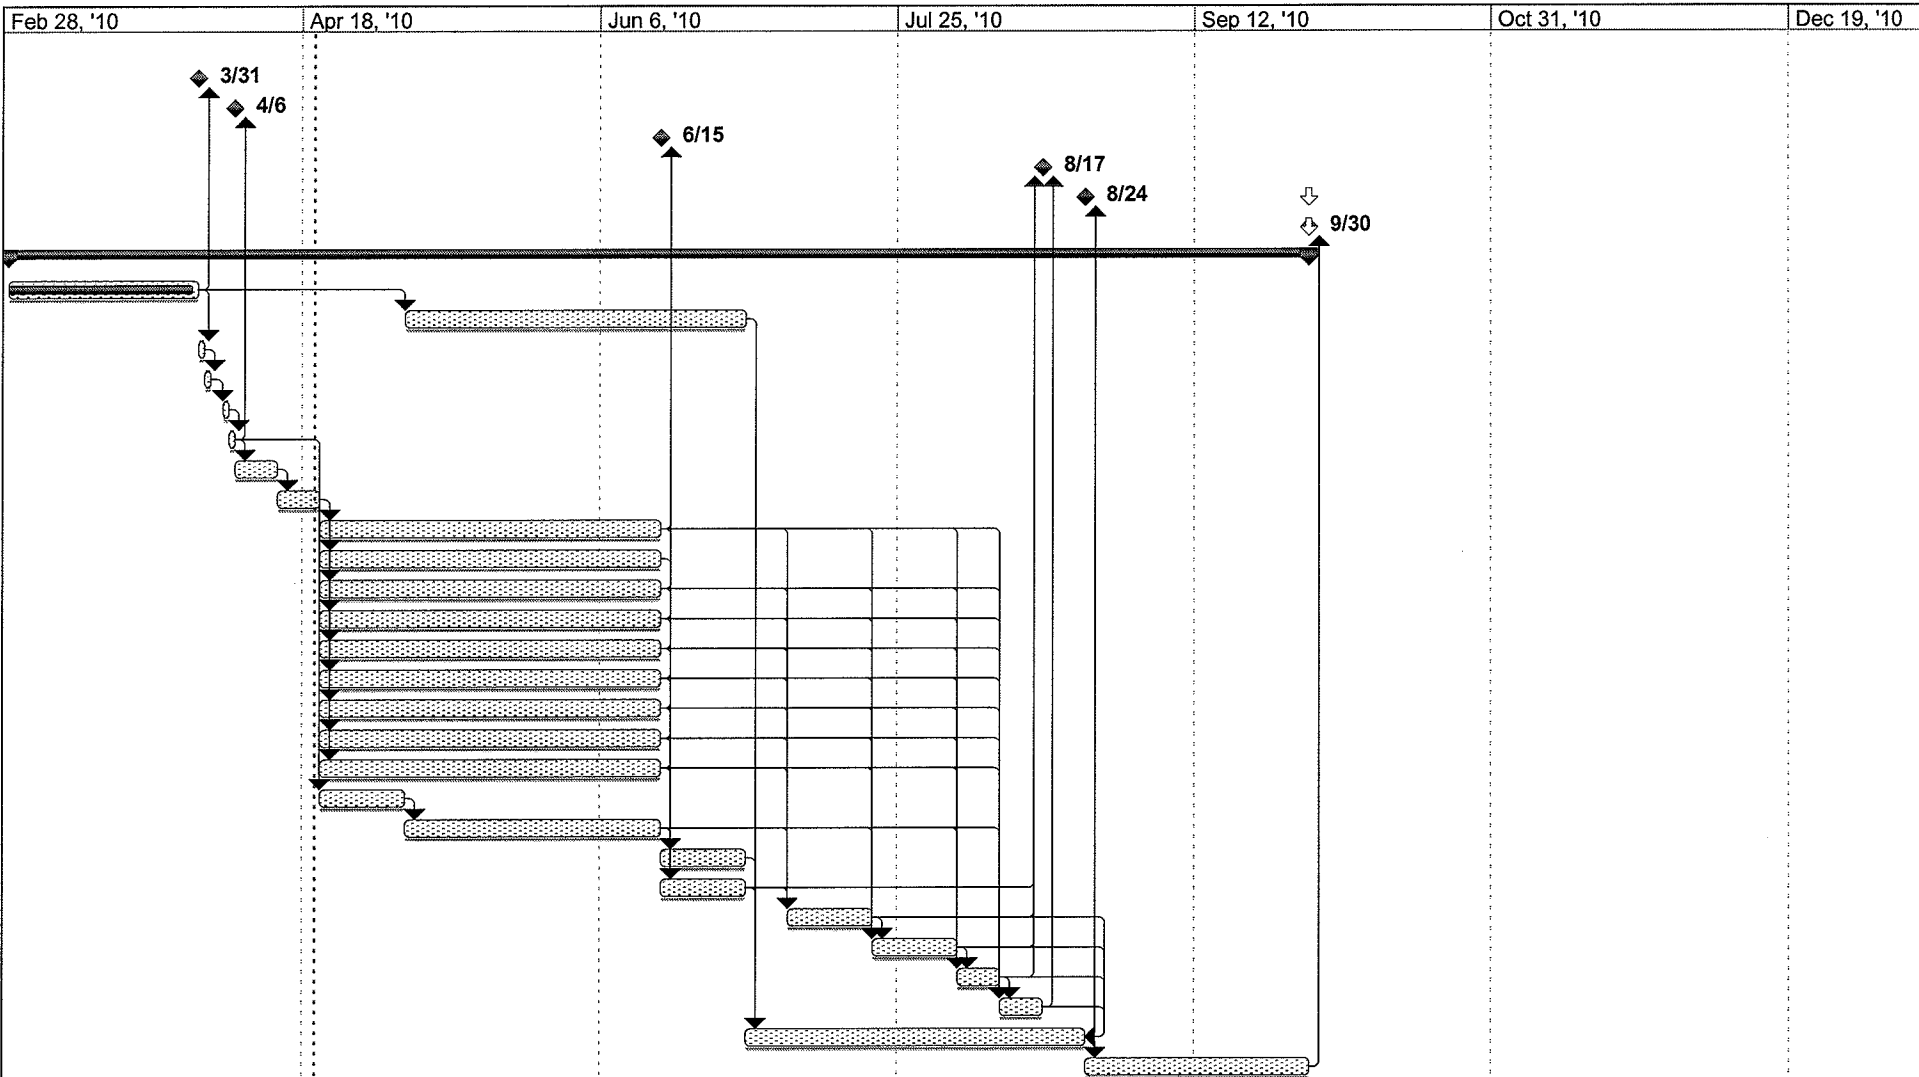

Project: GENI Deployment Schedule,
Date: Tue 4/20/10

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
